



Arlington High School Building Project

AHS Construction Update – October 5th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

COVID-19 Update


The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>

For more information, visit:
www.ahsbuilding.org

Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593

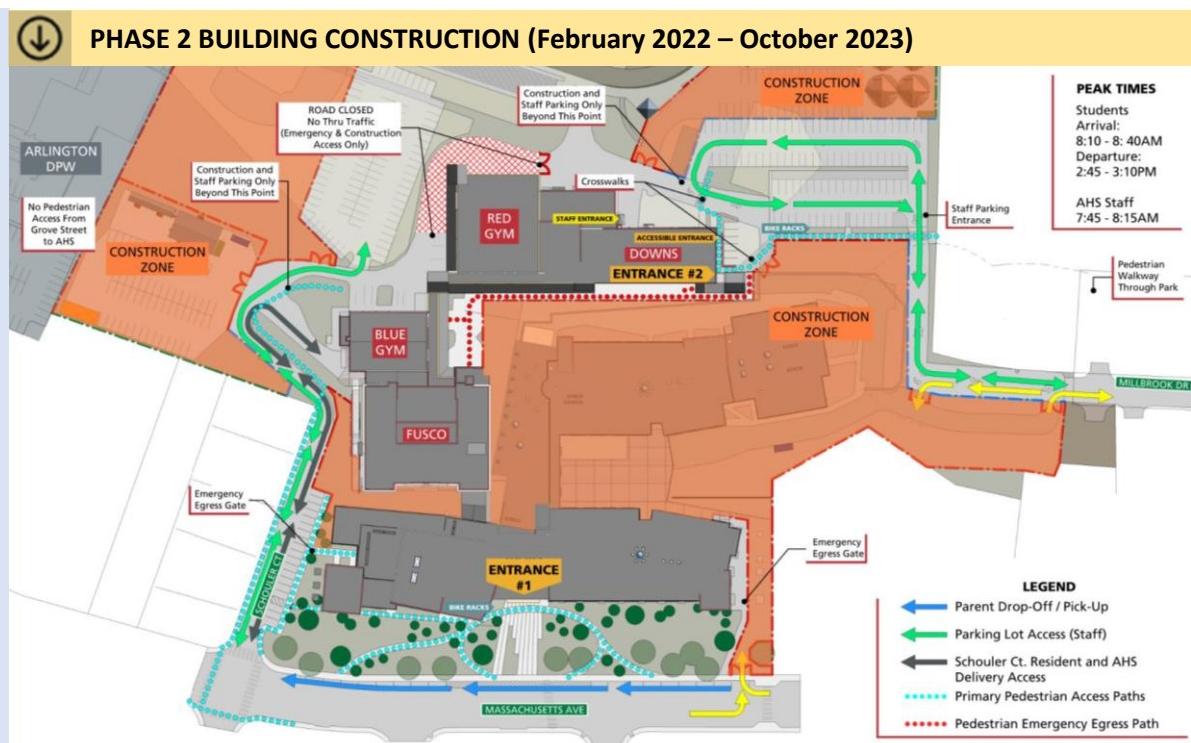

Construction Look Ahead – Week of October 9th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Phase 2:
 - Installation of masonry
 - Drywall installation, taping and sanding, and painting.
 - Installation of marker boards, bathroom partitions, and accessories
 - Installation of ceiling grids and ceiling tiles
 - Installation of casework and delivery of furniture
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinklers.
 - Installation of plumbing and electrical fixtures
 - Start-up and testing of mechanical units.
 - Grading of exterior site and loading dock area
 - Install of permanent Retaining Wall
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.



Skanska USA Inc.
Owner's Project Manager



Consigli Construction Co., Inc.
Construction Manager at Risk




HMFH Architects, Inc.
Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF OCTOBER 9TH, 2023




Photograph 1: Retaining Wall Progress

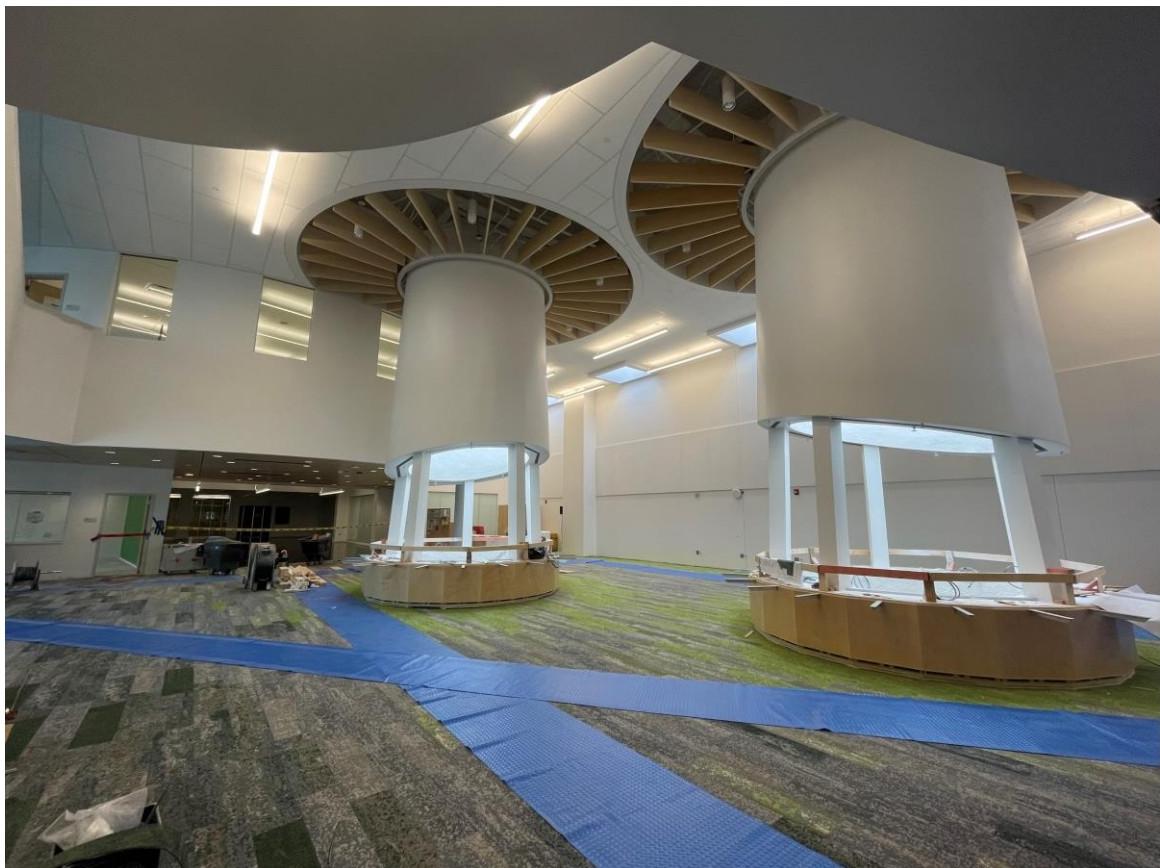

Photograph 2: Library Finishes Progress

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF OCTOBER 9TH, 2023

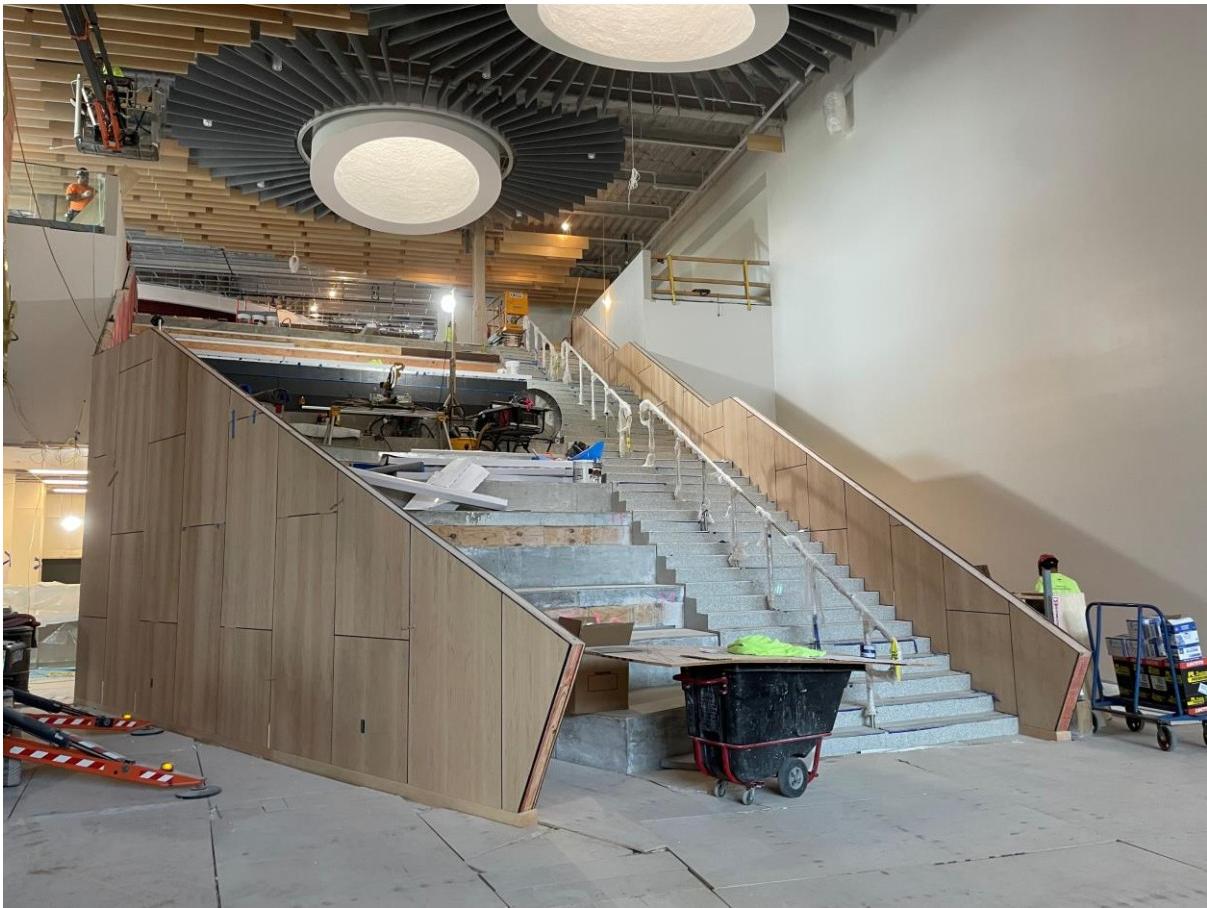

Photograph 3: Forum Stair Progress



Photograph 4: East Elevation (Mill Brook Dr)
